

# DRA ASTRA

## CONSTRUCTION UPDATE PHOTOS – MARCH 2026



## Content

- ❖ Master Plan
- ❖ Structure –Progress Status & Photos
  - ✓ Shell & Core
  - ✓ Block Work
  - ✓ Plastering
- ❖ Finishing –Progress Status & Photos
  - ✓ Toilet Waterproofing
  - ✓ Tile Laying
  - ✓ Painting
  - ✓ MEP Work
  - ✓ Upvc Windows
  - ✓ Joinery
- ❖ External Development

# STRUCTURE - PROGRESS STATUS & PHOTOS

DRA ASTRA				
PROGRESS STATUS				
S.No	Activity	Block -01		Remarks
1	Excavation	Completed		
2	Foundation	Completed		
3	Plinth Beam	Completed		
4	Back Filling	Completed		
5	Stilt Floor -Column	Completed		
6	Stilt Floor Roof Slab	Completed		
7	Block Work	Work in progress		
8	<b>First Floor</b>			
	Column	Completed		
	Roof Slab	Completed		
	Block Work	Work in progress		
	Plastering -Internal			
9	<b>Second Floor</b>			
	Column	Completed		
	Roof Slab	Completed		
	Block Work	Completed		
	Plastering -Internal	Work in progress		
10	<b>Third Floor</b>			
	Column	Completed		
	Roof Slab	Completed		
	Block Work	Completed		
	Plastering -Internal			
11	<b>Fourth Floor</b>			
	Column	Completed		
	Roof Slab	Completed		
	Block Work	Work in progress		
	Plastering -Internal			
12	<b>Fifth Floor</b>			
	Column	Completed		
	Roof Slab	Completed		
	Block Work	Work in progress		
	Plastering -Internal			
13	<b>Sixth Floor</b>			
	Column	Completed		
	Roof Slab	Work in progress		
	Block Work			
	Plastering -Internal			
14	<b>Seventh Floor</b>			
	Column	Work in progress		
	Roof Slab	Work in progress		
	Block Work			
	Plastering -Internal			



**MASTER PLAN**

## SOUTHEAST SIDE ELEVATION



## NORTH WEST SIDE ELEVATION



## Northeast SIDE ELEVATION



## SOUTH SIDE ELEVATION



# North SIDE ELEVATION



# 5<sup>th</sup> floor roof Pour 2 slab concrete work completed.



## Main Building – 6<sup>th</sup> floor roof Pour 1 roof slab Reinforcement and Electrical work completed



# Main Building – 6<sup>th</sup> floor roof Pour 1 roof slab concrete completed





OPPO K13 5G  
Chennai | 27 March 2026 at 16:37

# Main Building – 6<sup>th</sup> floor roof Pour 2 roof Reinforcement & Electrical work completed



## 7th floor column concrete work (44 Nos / 66 Nos)



## 7th floor roof slab shuttering work in progress.



**3rd floor BW 100% completed & 4<sup>th</sup> floor BW 65% completed**




## 2<sup>nd</sup> floor internal flat plastering & 3<sup>rd</sup> floor electrical work in progress



## Mock-up flat internal plumbing & ceiling putty work in progress



## Mock-up flat sunken filling work completed

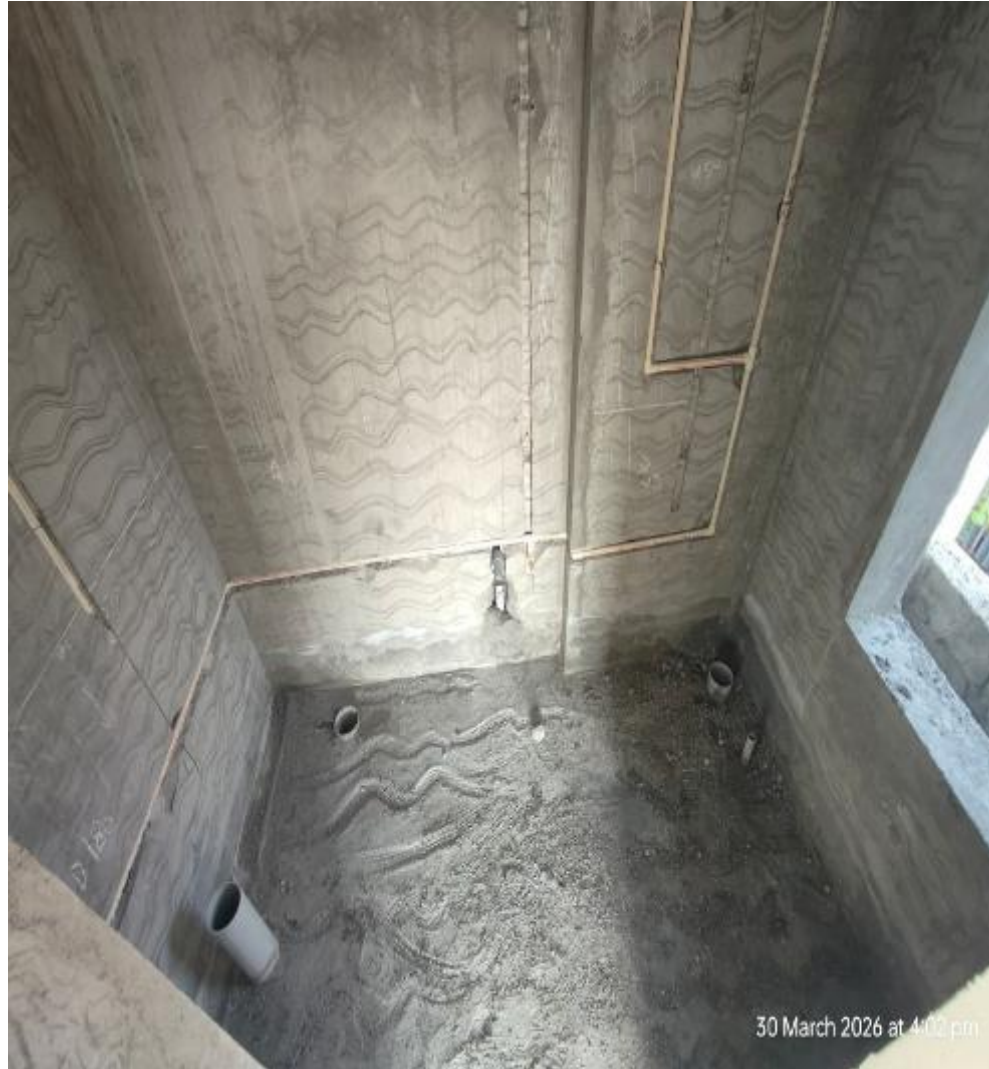

*Thank  
you!*
