



**DRA INFINIQUE**  
**CONSTRUCTION UPDATES AUG -25**





**North Side View**





**East Side View.**





**South Side View.**





**Front view.**





**101 Mock up flat waterproofing work completed.**





**101 Mock up flat toilet plumbing work completed.**





**101 Mock up flat toilet ledge wall construction completed.**





**101 Mock up flat Flooring and POP Laying work completed.**





**101 Mock up flat door fixing work completed.**





**101 Mock up flat UPVC Window fixing work completed.**





**101 Muck up flat final painting work in progress.**





**101 Sales Office flat tile laying work in progress.**





**First floor inner wall plastering work completed.**





**First floor outer plastering work in progress.**





**2<sup>nd</sup> Floor plastering work in progress.**





**4<sup>th</sup> Floor block work completed.**





**5th Floor cleaning work completed.**





**5th Floor block work in progress.**





**Pour 2 – 6<sup>th</sup> Floor roof reinforcement work completed.**





**Pour 2 – 6<sup>th</sup> Floor roof electrical conduit work completed.**





**Pour 2 – 6<sup>th</sup> Floor roof slab concrete work completed.**





**Pour 2 – 7<sup>th</sup> Floor column concrete work completed (22/22).**





**Pour 2 – 7<sup>th</sup> Floor roof shuttering work completed.**





**Pour 2 – 7<sup>th</sup> Floor roof reinforcement work completed.**





**Pour 2 – 7<sup>th</sup> Floor roof electrical conduit laying work completed.**





**Pour 2 – 7<sup>th</sup> Floor roof concrete work completed.**





**Pour 2 – 7<sup>th</sup> Floor roof concrete curing work.**





**Pour 1 – 8<sup>th</sup> Floor column reinforcement work completed (45/45).**





**Pour 1 – 8<sup>th</sup> Floor column concrete work completed (45/45).**





**Pour 1 – 8<sup>th</sup> Floor column curing work completed.**





**Pour 1 – 8<sup>th</sup> Floor roof shuttering work completed.**





**Pour 1 – 8<sup>th</sup> Floor roof reinforcement work completed.**





**Pour 1 – 8<sup>th</sup> Floor roof slab concrete work completed.**





**Pour 1 – 8<sup>th</sup> Floor roof slab curing work completed.**





**Pour 1 – 8<sup>th</sup> Floor column reinforcement work completed (45/45).**





**Pour 2 – 8<sup>th</sup> Floor column concrete work completed.**





**Pour 1 – 9<sup>th</sup> Floor column reinforcement work completed (45/45).**





**Pour 1 – 9<sup>th</sup> Floor column concrete work completed (45/45).**





**Pour 1 – 9<sup>th</sup> Floor roof shuttering work completed.**





**Pour 1 – 9<sup>th</sup> Floor roof reinforcement work completed.**





**Pour 1 – 9<sup>th</sup> Floor roof electrical conduit laying work in progress.**






**Debris chute installation work completed.**






**Tower -2 Commercial block basement roof slab curing work completed.**



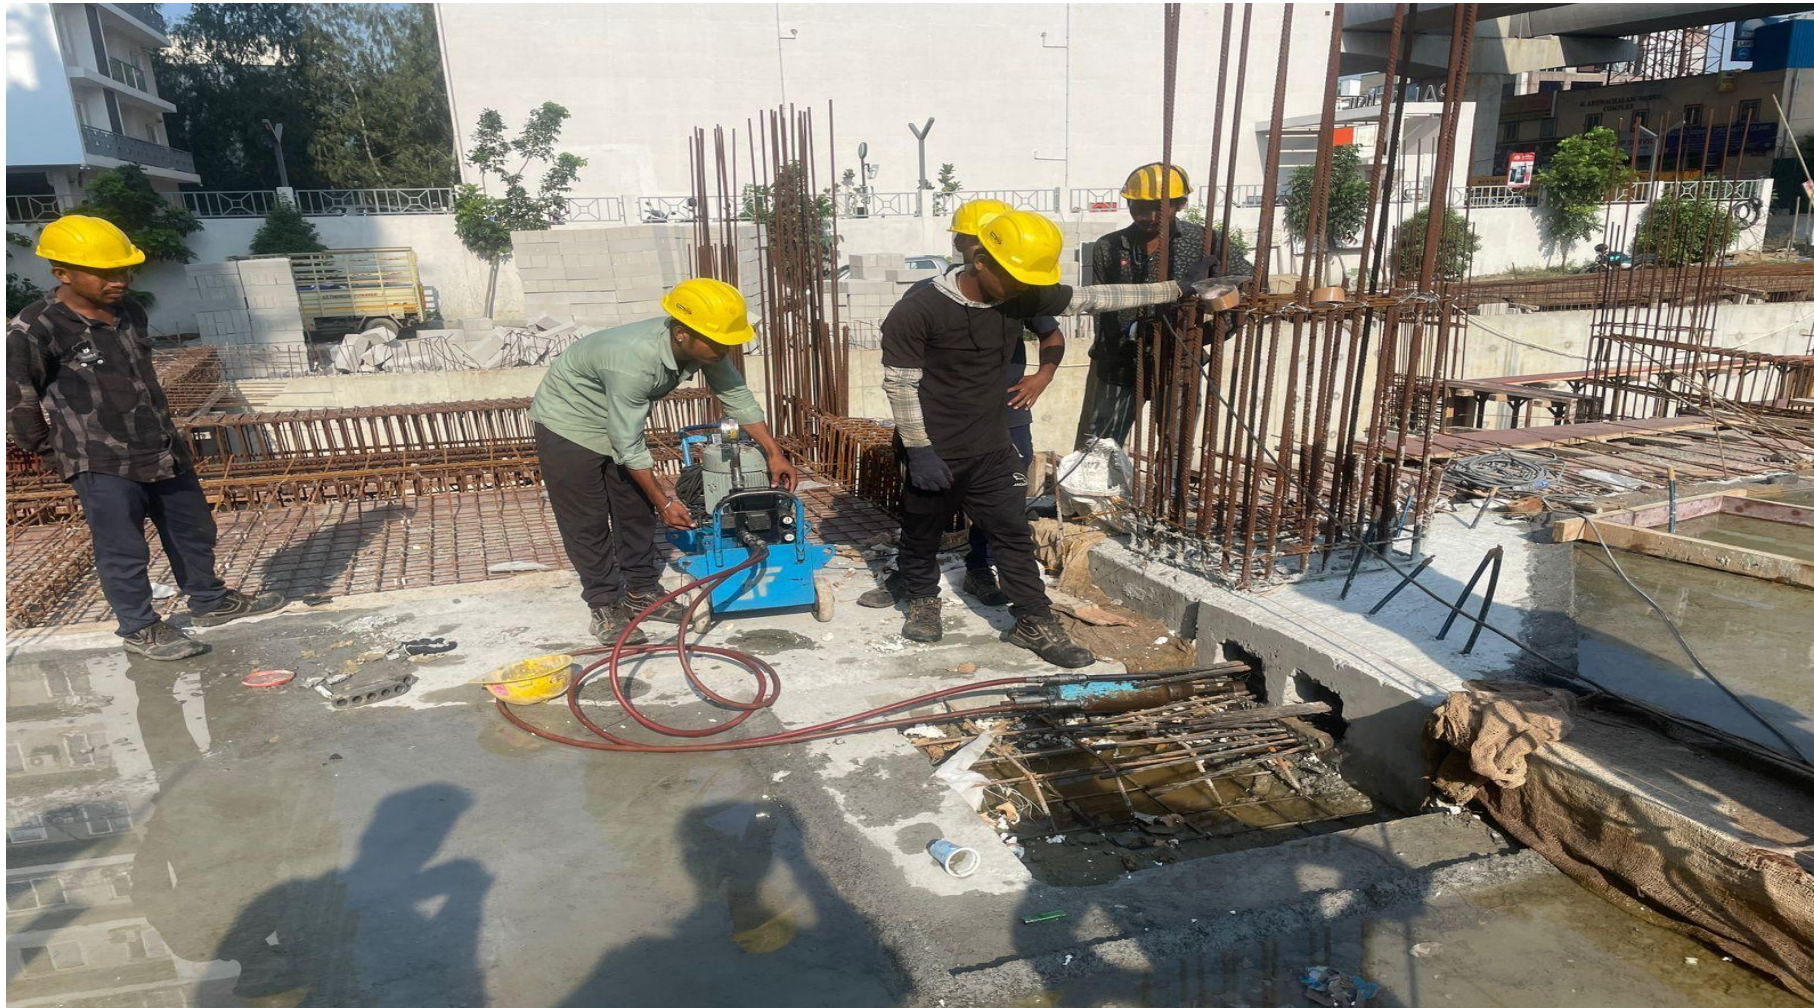

**Tower -2 Commercial basement roof Tendon stressing work completed.**



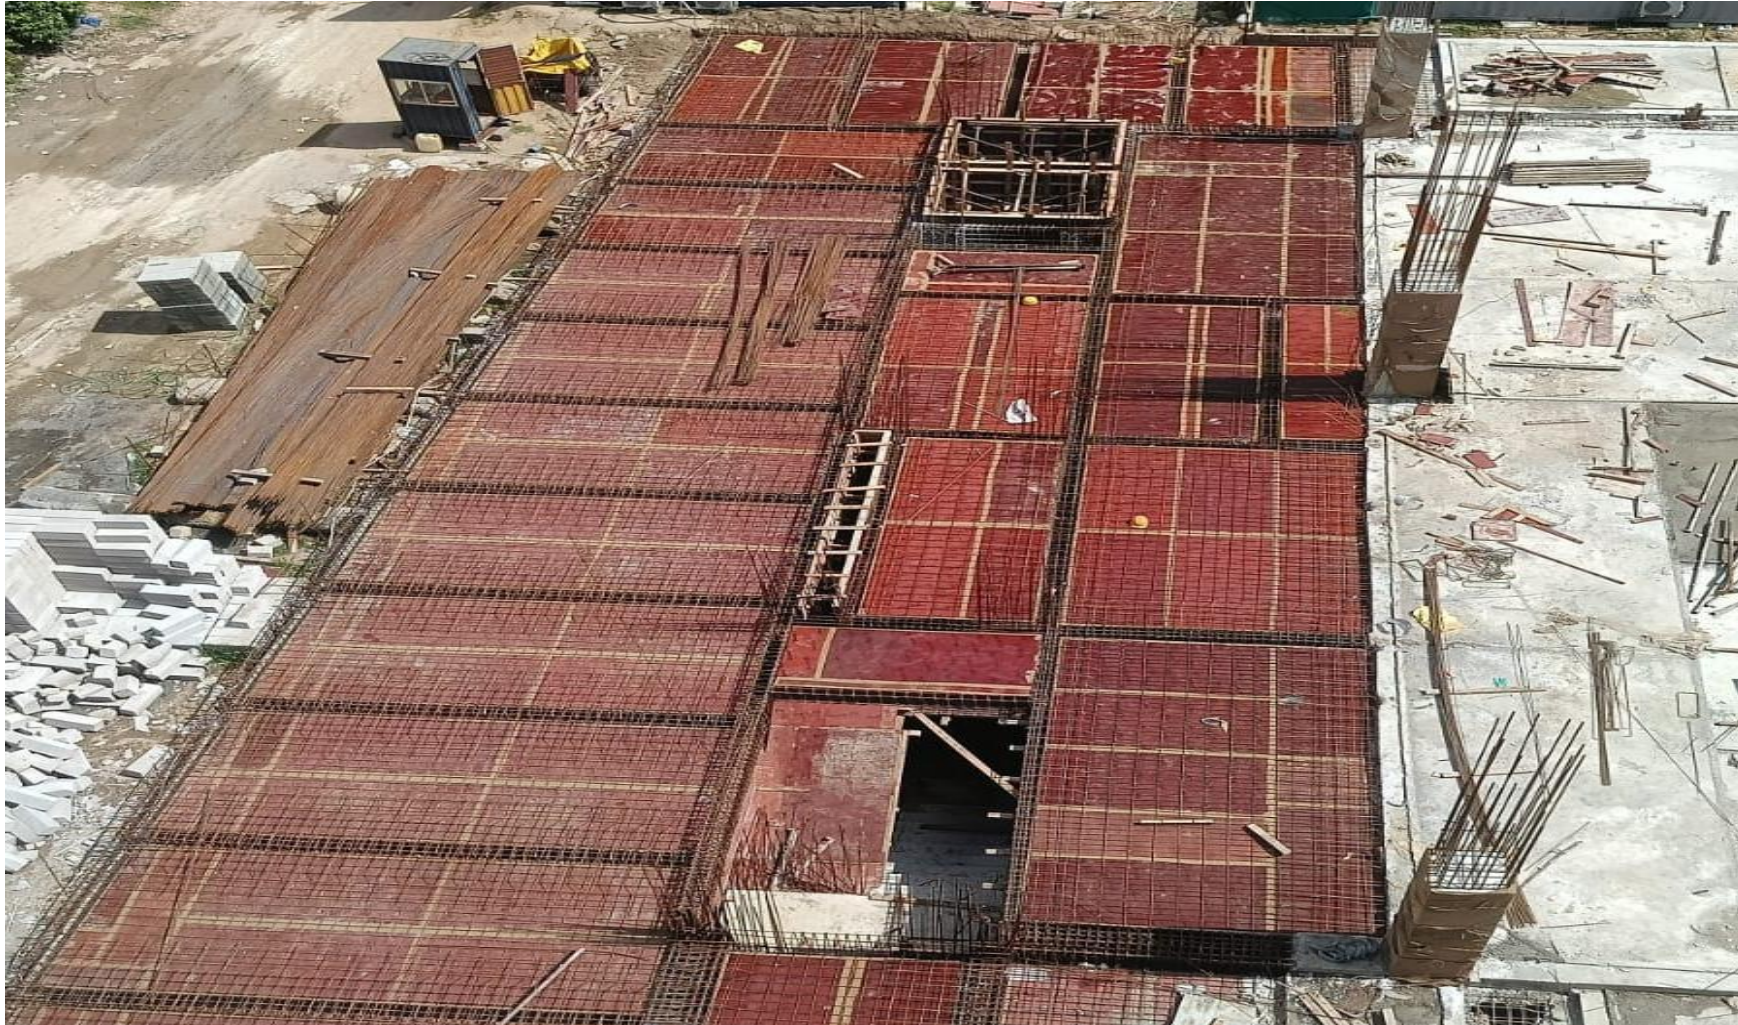

**Tower -2 P2 Basement roof shuttering work completed .**





**Tower -2 P2 Basement roof reinforcement work completed .**





**Tower -2 P2 Basement roof concrete work completed .**





**Tower -2 P2 Basement roof curing work in progress .**





**Tower -2 Stilt floor P1 PT Beam soffit shuttering work in progress .**



# DRA INFINIQUE PROJECT COMPLETION UPDATES

S NO	Description	Unit	Total qty	Completed qty	% of Completion
1	T-1 Basement roof slab	Cum	497	497	100%
2	T-1 First floor roof slab	Cum	216	216	100%
3	T-1 Second floor roof slab	Cum	216	216	100%
4	T-1 Third floor roof slab	Cum	220	220	100%
5	T-1 Fourth floor roof slab	Cum	220	220	100%
6	T-1 Fifth floor roof slab	Cum	220	220	100%
7	T-1 Sixth floor roof slab	Cum	220	200	100%
8	T-1 Seventh floor roof slab	Cum	220	220	100%
9	T-1 Eighth floor roof slab	Cum	220	143	66%
10	T-2 P1 Basement roof slab	Cum	198	198	100%
11	T-2 P2 Basement roof slab	Cum	125	125	100%



*Thank  
you!*
