



**DRA INFINIQUE**  
**CONSTRUCTION UPDATES OCTOBER -25.**



**North Side View**



**East Side View.**



**South Side View.**



**Front view.**



**MOCKUP FLAT - MAIN DOOR**



**FOYER**



**TV UNIT**



**LIVING**



**DINING**



**DINING WASH BASIN**



**KITCHEN**



**BALCONY**



**MASTER BEDROOM**



**MASTER BEDROOM TOILET**



**BED ROOM 1**



**BED ROOM 1 TOILET**



**BED ROOM 2**



**BED ROOM 2 TOILET**



**102 Sales Office flat door fixing work completed.**



**102 Sales Office flat Window fixing work completed.**



**102 Sales Office flat handrail fixing work completed.**



**2<sup>nd</sup> Floor toilet waterproofing work completed.**



**1<sup>st</sup> floor corridor plastering work completed.**



**2<sup>nd</sup> Floor corridor inner plastering work completed.**



**3<sup>rd</sup> Floor toilet waterproofing work in progress.**



**3<sup>rd</sup> floor inner wall plastering work completed.**



**3<sup>rd</sup> Floor corridor inner plastering work completed.**



**4<sup>th</sup> Floor electrical wall chasing work in progress.**



**4<sup>th</sup> floor inner wall plastering work completed**



**4<sup>th</sup> floor inner wall plastering work in progress.**



**4<sup>th</sup> floor toilet water proofing work in progress**



**5<sup>th</sup> Floor plastering work in progress.**



**6<sup>th</sup> Floor block work completed.**



**7<sup>th</sup> Floor block work completed.**



**8<sup>th</sup> Floor block work in progress.**



**9<sup>th</sup> Floor block work in progress.**



**Pour 2 – 10<sup>th</sup> Floor column concrete work completed.**



**Pour 2 – 10<sup>th</sup> Floor roof reinforcement work completed.**



**Pour 2 – 10<sup>th</sup> Floor roof electrical conduit laying work completed.**



**Pour 2 – 10<sup>th</sup> Floor roof concrete work completed.**




**Pour 1 – 11<sup>th</sup> floor column reinforcement work completed.**



**Pour 1 – 11<sup>th</sup> floor column concrete work completed**



**Pour 1 – 11<sup>th</sup> Floor roof reinforcement work completed.**

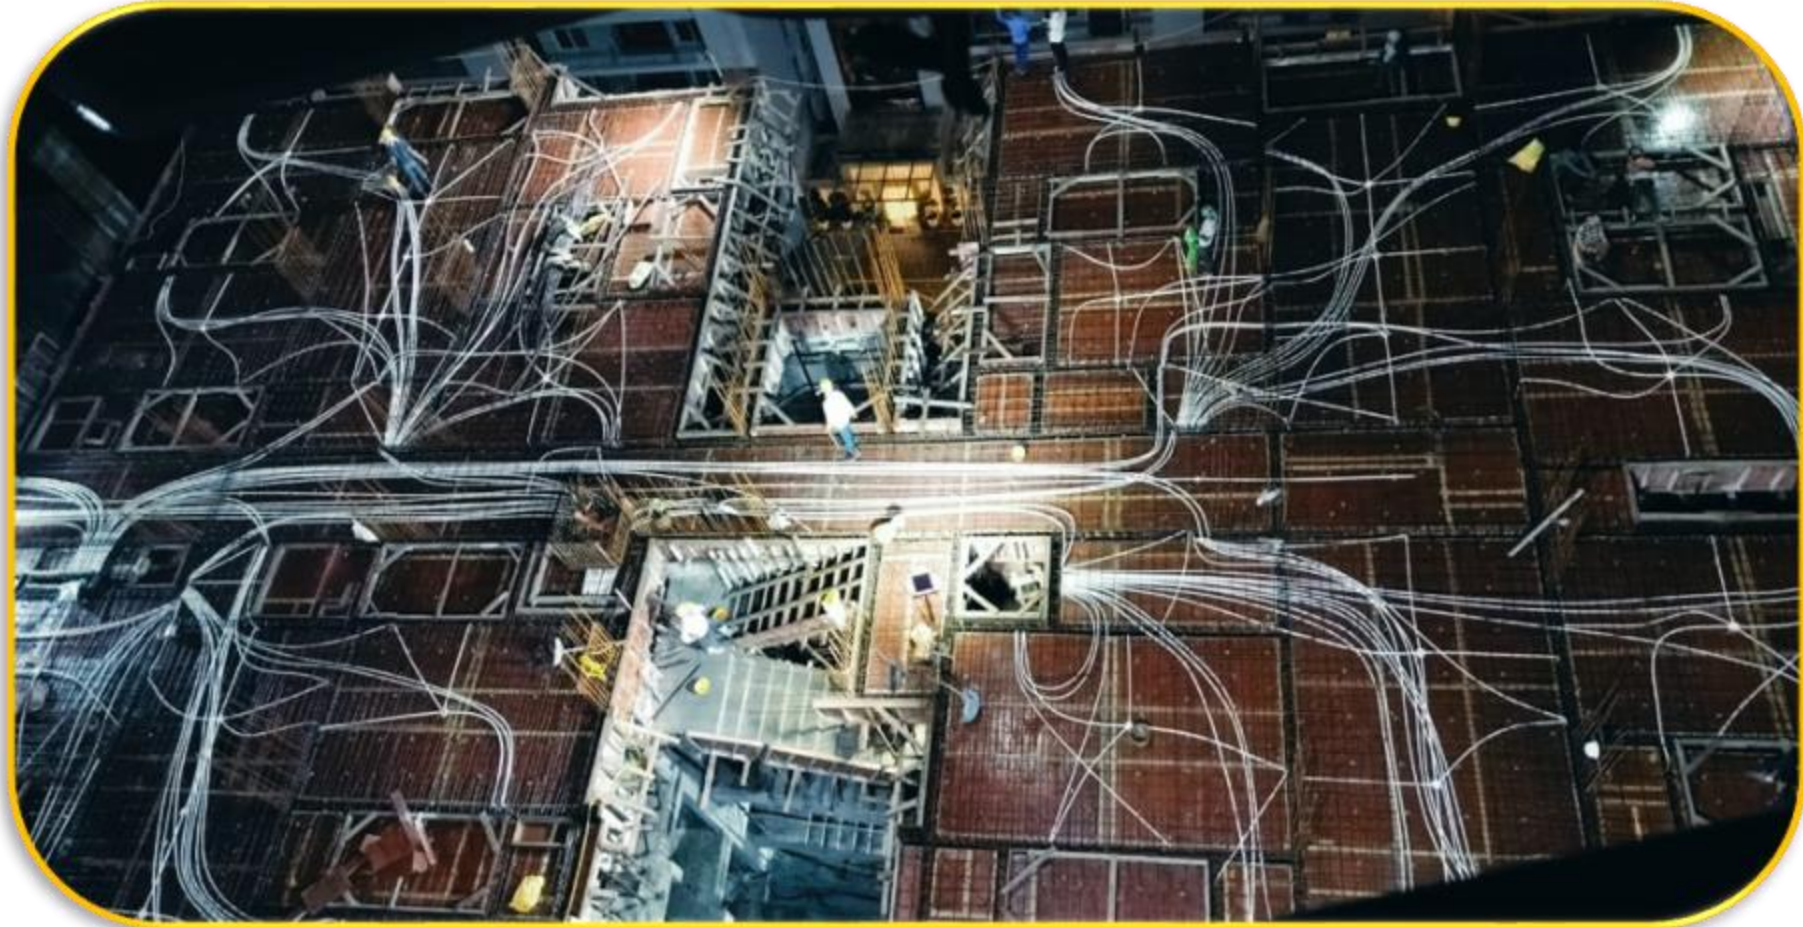

**Pour 1 – 11<sup>th</sup> Floor roof electrical conduit laying work completed.**



**Pour 1 – 11<sup>th</sup> Floor roof concrete work completed.**



**Pour 2 – 11<sup>th</sup> Floor roof reinforcement work completed.**



**Pour 2 – 11<sup>th</sup> Floor roof electrical conduit laying work completed.**



**Pour 2 – 11<sup>th</sup> Floor roof concrete work completed.**



**Pour 1 – 12<sup>th</sup> floor column reinforcement work completed.**



**Pour 1 – 12<sup>th</sup> floor column shuttering work in progress.**



**Pour 1 – 12<sup>th</sup> floor column concrete work in progress**



**Pour 1 – 12<sup>th</sup> floor roof shuttering work in progress.**



**Pore 2 - 12<sup>th</sup> floor column reinforcement work in progress**



**Tower -2 stilt floor roof slab curing work completed.**



**Tower -2 stilt floor roof PT strand stressing work completed.**



**Tower -2 first floor column reinforcement work completed .**



**Tower 2 1<sup>st</sup> floor column concrete work completed**



**Tower 2 1<sup>st</sup> floor roof shuttering work in progress**

### DRA INFINIQUE PROJECT COMPLETION UPDATES

| S NO | Description                  | Unit | Total qty | Completed qty | % of Completion |
|------|------------------------------|------|-----------|---------------|-----------------|
| 1    | T-1 Basement roof slab       | Cum  | 497       | 497           | 100%            |
| 2    | T-1 First floor roof slab    | Cum  | 216       | 216           | 100%            |
| 3    | T-1 Second floor roof slab   | Cum  | 216       | 216           | 100%            |
| 4    | T-1 Third floor roof slab    | Cum  | 220       | 220           | 100%            |
| 5    | T-1 Fourth floor roof slab   | Cum  | 220       | 220           | 100%            |
| 6    | T-1 Fifth floor roof slab    | Cum  | 220       | 220           | 100%            |
| 7    | T-1 Sixth floor roof slab    | Cum  | 220       | 200           | 100%            |
| 8    | T-1 Seventh floor roof slab  | Cum  | 220       | 220           | 100%            |
| 9    | T-1 Eighth floor roof slab   | Cum  | 220       | 220           | 100%            |
| 10   | T-1 Ninth floor roof slab    | Cum  | 220       | 220           | 100%            |
| 11   | T-1 Tenth floor roof slab    | Cum  | 220       | 220           | 100%            |
| 12   | T-1 Eleventh floor roof slab | Cum  | 220       | 220           | 100%            |
| 13   | T-2 P1 Basement roof slab    | Cum  | 198       | 198           | 100%            |
| 14   | T-2 P2 Stilt roof slab       | Cum  | 125       | 125           | 100%            |

*Thank  
you!*
