

DRA ASTRA

MONTHLY CONSTRUCTION PHOTOS – JUNE 2026



Content

- ❖ Master Plan
- ❖ Structure –Progress Status & Photos
 - ✓ Shell & Core
 - ✓ Block Work
 - ✓ Plastering
- ❖ Finishing –Progress Status & Photos
 - ✓ Toilet Waterproofing
 - ✓ Tile Laying
 - ✓ Painting
 - ✓ MEP Work
 - ✓ Upvc Windows
 - ✓ Joinery
- ❖ External Development

STRUCTURE - PROGRESS STATUS & PHOTOS

DRA ASTRA			
PROGRESS STATUS			
S.No	Activity	Block -01	Remarks
1	Excavation	Completed	
2	Foundation	Completed	
3	Plinth Beam	Completed	
4	Back Filling	Completed	
5	Stilt Floor -Column	Completed	
6	Stilt Floor Roof Slab	Completed	
7	Block Work	Work in progress	
8	First Floor		
	Column	Completed	
	Roof Slab	Completed	
	Block Work	Work in progress	
	Plastering -Internal		
9	Second Floor		
	Column	Completed	
	Roof Slab	Completed	
	Block Work	Completed	
	Plastering -Internal	Work in progress	
10	Third Floor		
	Column	Completed	
	Roof Slab	Completed	
	Block Work	Completed	
	Plastering -Internal	Work in progress	
11	Fourth Floor		
	Column	Completed	
	Roof Slab	Completed	
	Block Work	Completed	
	Plastering -Internal	Work in progress	
12	Fifth Floor		
	Column	Completed	
	Roof Slab	Completed	
	Block Work	Work in progress	
	Plastering -Internal		
13	Sixth Floor		
	Column	Completed	
	Roof Slab	Completed	
	Block Work	Work in progress	
	Plastering -Internal		
14	Seventh Floor		
	Column	Completed	
	Roof Slab	Completed	
	Block Work		
	Plastering -Internal		
15	Eighth Floor		
	Column	Completed	
	Roof Slab	Completed	
	Block Work		
	Plastering -Internal		
16	Ninth Floor		
	Column	Work in progress	
	Roof Slab	Work in progress	
	Block Work		
	Plastering -Internal		
13	Above Terrace		
	Parapet		
	OHT		
	LMR		
	SHR		



MASTER PLAN

SOUTHEAST SIDE ELEVATION



NORTHWEST SIDE ELEVATION



NORTHEAST SIDE ELEVATION



SOUTH SIDE ELEVATION



WEST SIDE ELEVATION



Main Building – 8th floor roof Pour 1 roof slab Reinforcement & Electrical work completed.



Main Building – Pour 1 - 8th floor roof slab concrete work completed.



Main building - Pour 1 - 9th floor column concrete work (64 Nos / 66 Nos)




Main building - Pour 1 - 9th floor roof shuttering work in progress.



Main building - Pour 2 - 8th floor column concrete work in progress (59 Nos / 59 Nos)



Main building - Pour 2 - 8th floor roof slab shuttering work completed.

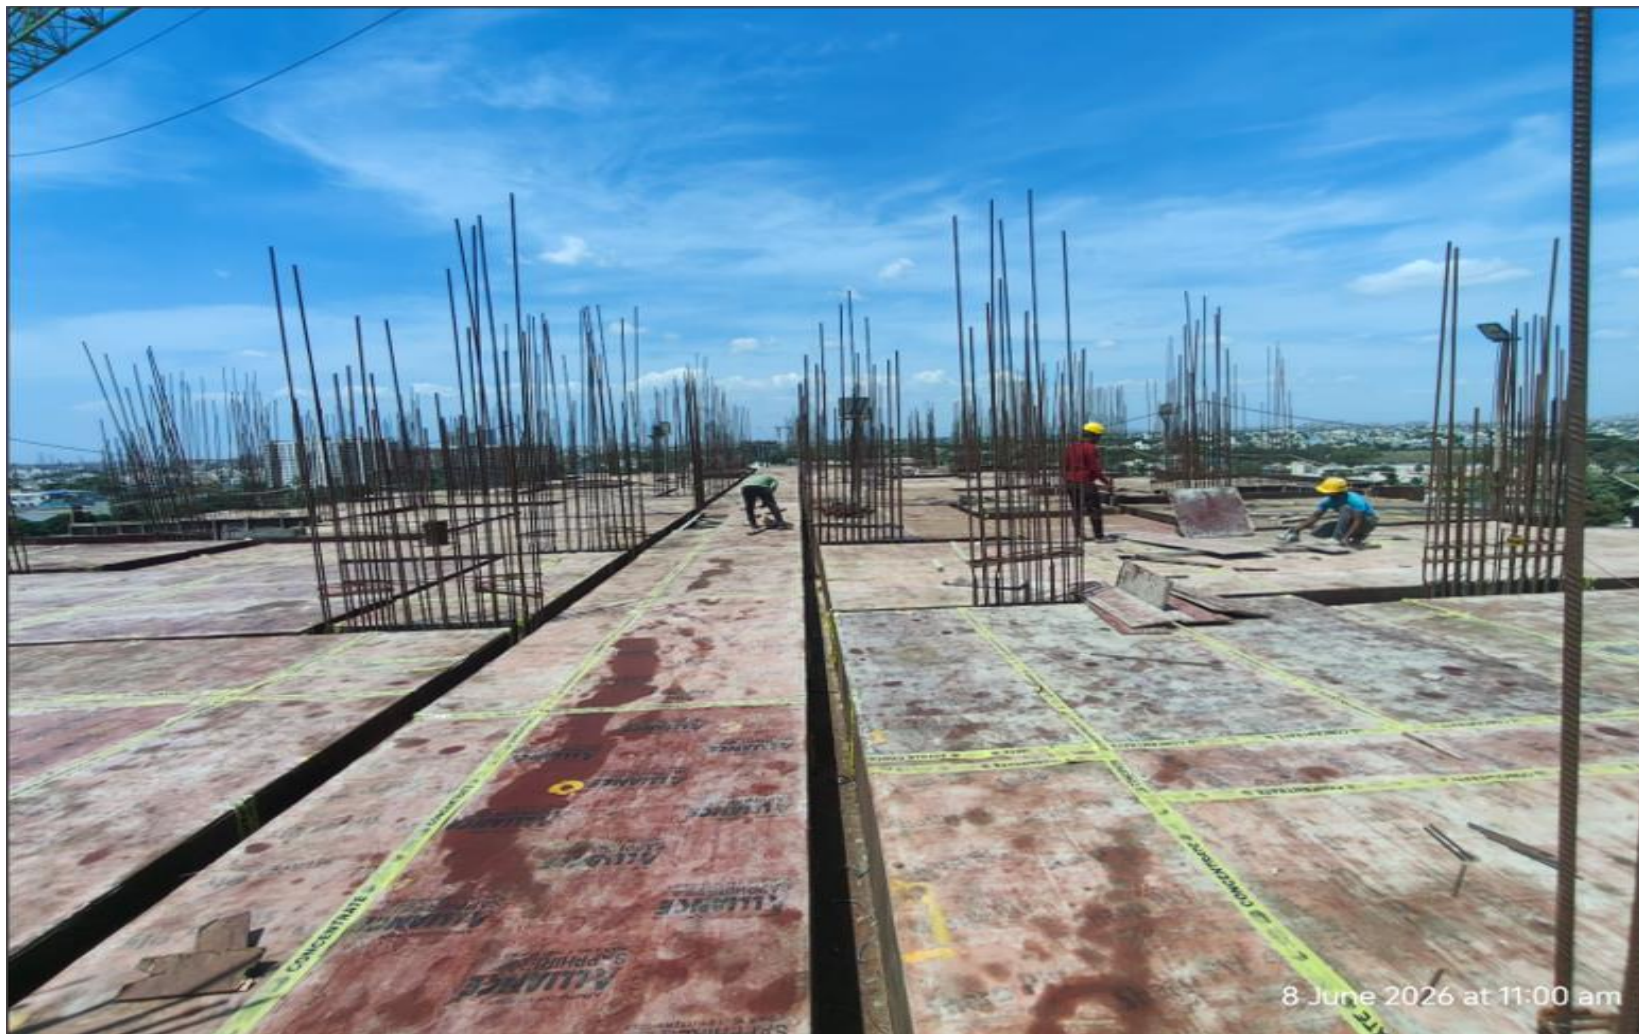

Main building - Pour 2 - 8th floor roof slab Reinforcement and Electrical work completed.



Main building - Pour 2 - 8th floor roof slab concrete work completed.



Main building - Pour 1 - 9th floor column reinforcement work (25 Nos / 59 Nos)



5th floor blockwork in progress (80% completed)



6th floor blockwork in progress (60% completed)



5th floor Electrical wall chasing work in progress.



2nd & 3rd floor internal plastering work in progress.



4th floor toilet plastering work completed.



2nd & 3rd floor water proofing and sunken filling work in progress.



Mock-up flat false ceiling work completed & Painting work in progress.



Thank
you!
