



DRA HARMONY
CONSTRUCTION UPDATES – OCTOBER 2024

STAGE COMPLETION STATUS UP TO OCTOBER-24

S. No	Description	Status	Remarks
1	Completion of Foundation	Completed	
2	Completion of Stilt Floor Roof	Completed	
3	Completion of Upper Stilt Floor Roof	Completed	
4	Completion of First Floor Roof	Completed	
5	Completion of Third Floor Roof	Completed	
6	Completion of Fifth Floor Roof	Completed	
7	Completion of Seventh Floor Roof	Completed	
8	Completion of Ninth Floor Roof	Completed	
9	Completion of Eleventh Floor Roof		
10	Completion of Thirteenth Floor Roof		
11	Completion of Masonry Work	Upto 7 th Floor Completed	
12	Completion of Internal Plastering	Upto 2 nd Floor Completed	
13	Completion of Internal Finishes		



Main Building – Tenth Floor Slab Concrete Work Completed



Main Building – Tenth Floor Slab Curing Work In Progress



Main Building – Eighth Floor Hacking & Surface Grinding Work In Progress



Main Building – Seventh Floor Block Work Completed



Main Building – Eighth Floor Block Work In Progress



Main Building – First Floor Internal Wall Plastering Work Completed



Main Building – Second Floor Internal Wall Plastering Work Completed




Main Building – Third Floor Internal Wall Plastering Work In progress



Main Building –Fourth Floor Kitchen Counter Slab Work In Progress



Electrical – Fourth Floor Wall Chasing Completed

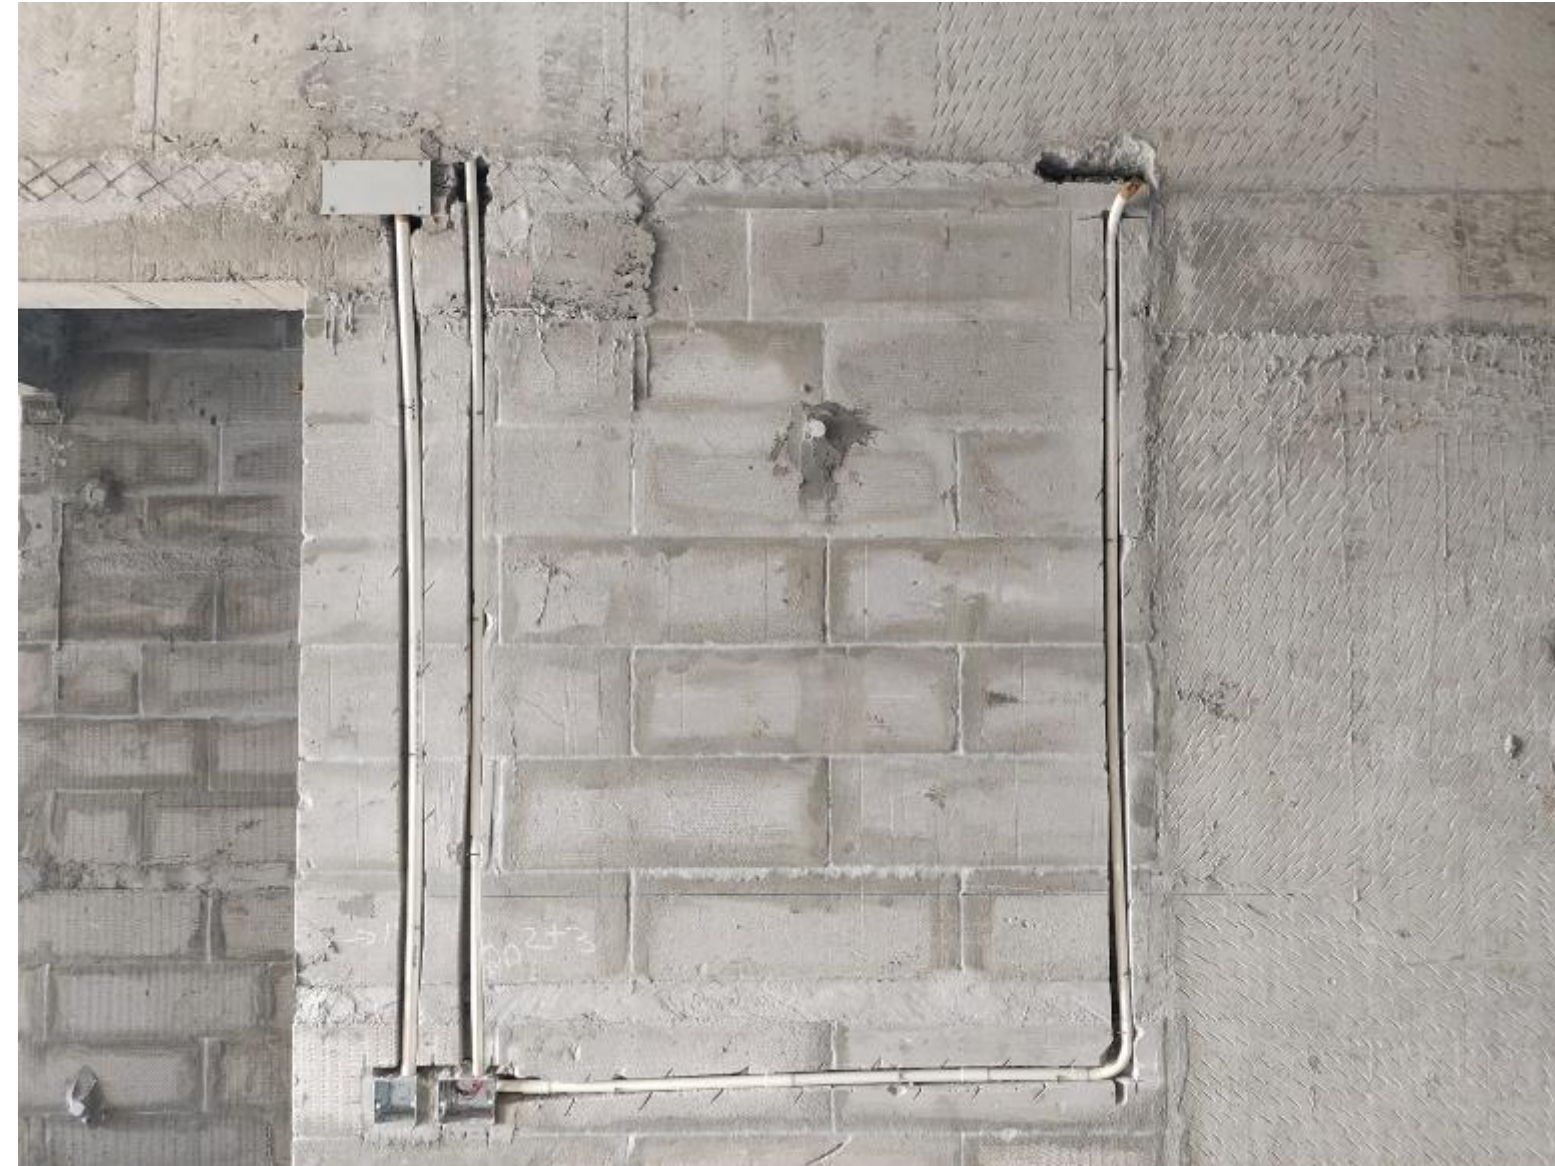


Electrical – Fifth Floor Wall Chasing Work In Progress



Plumbing – Sixth Floor AC Sleeve Fixing Work Completed



Plumbing – First Floor Toilet Wall Chasing Work In Progress

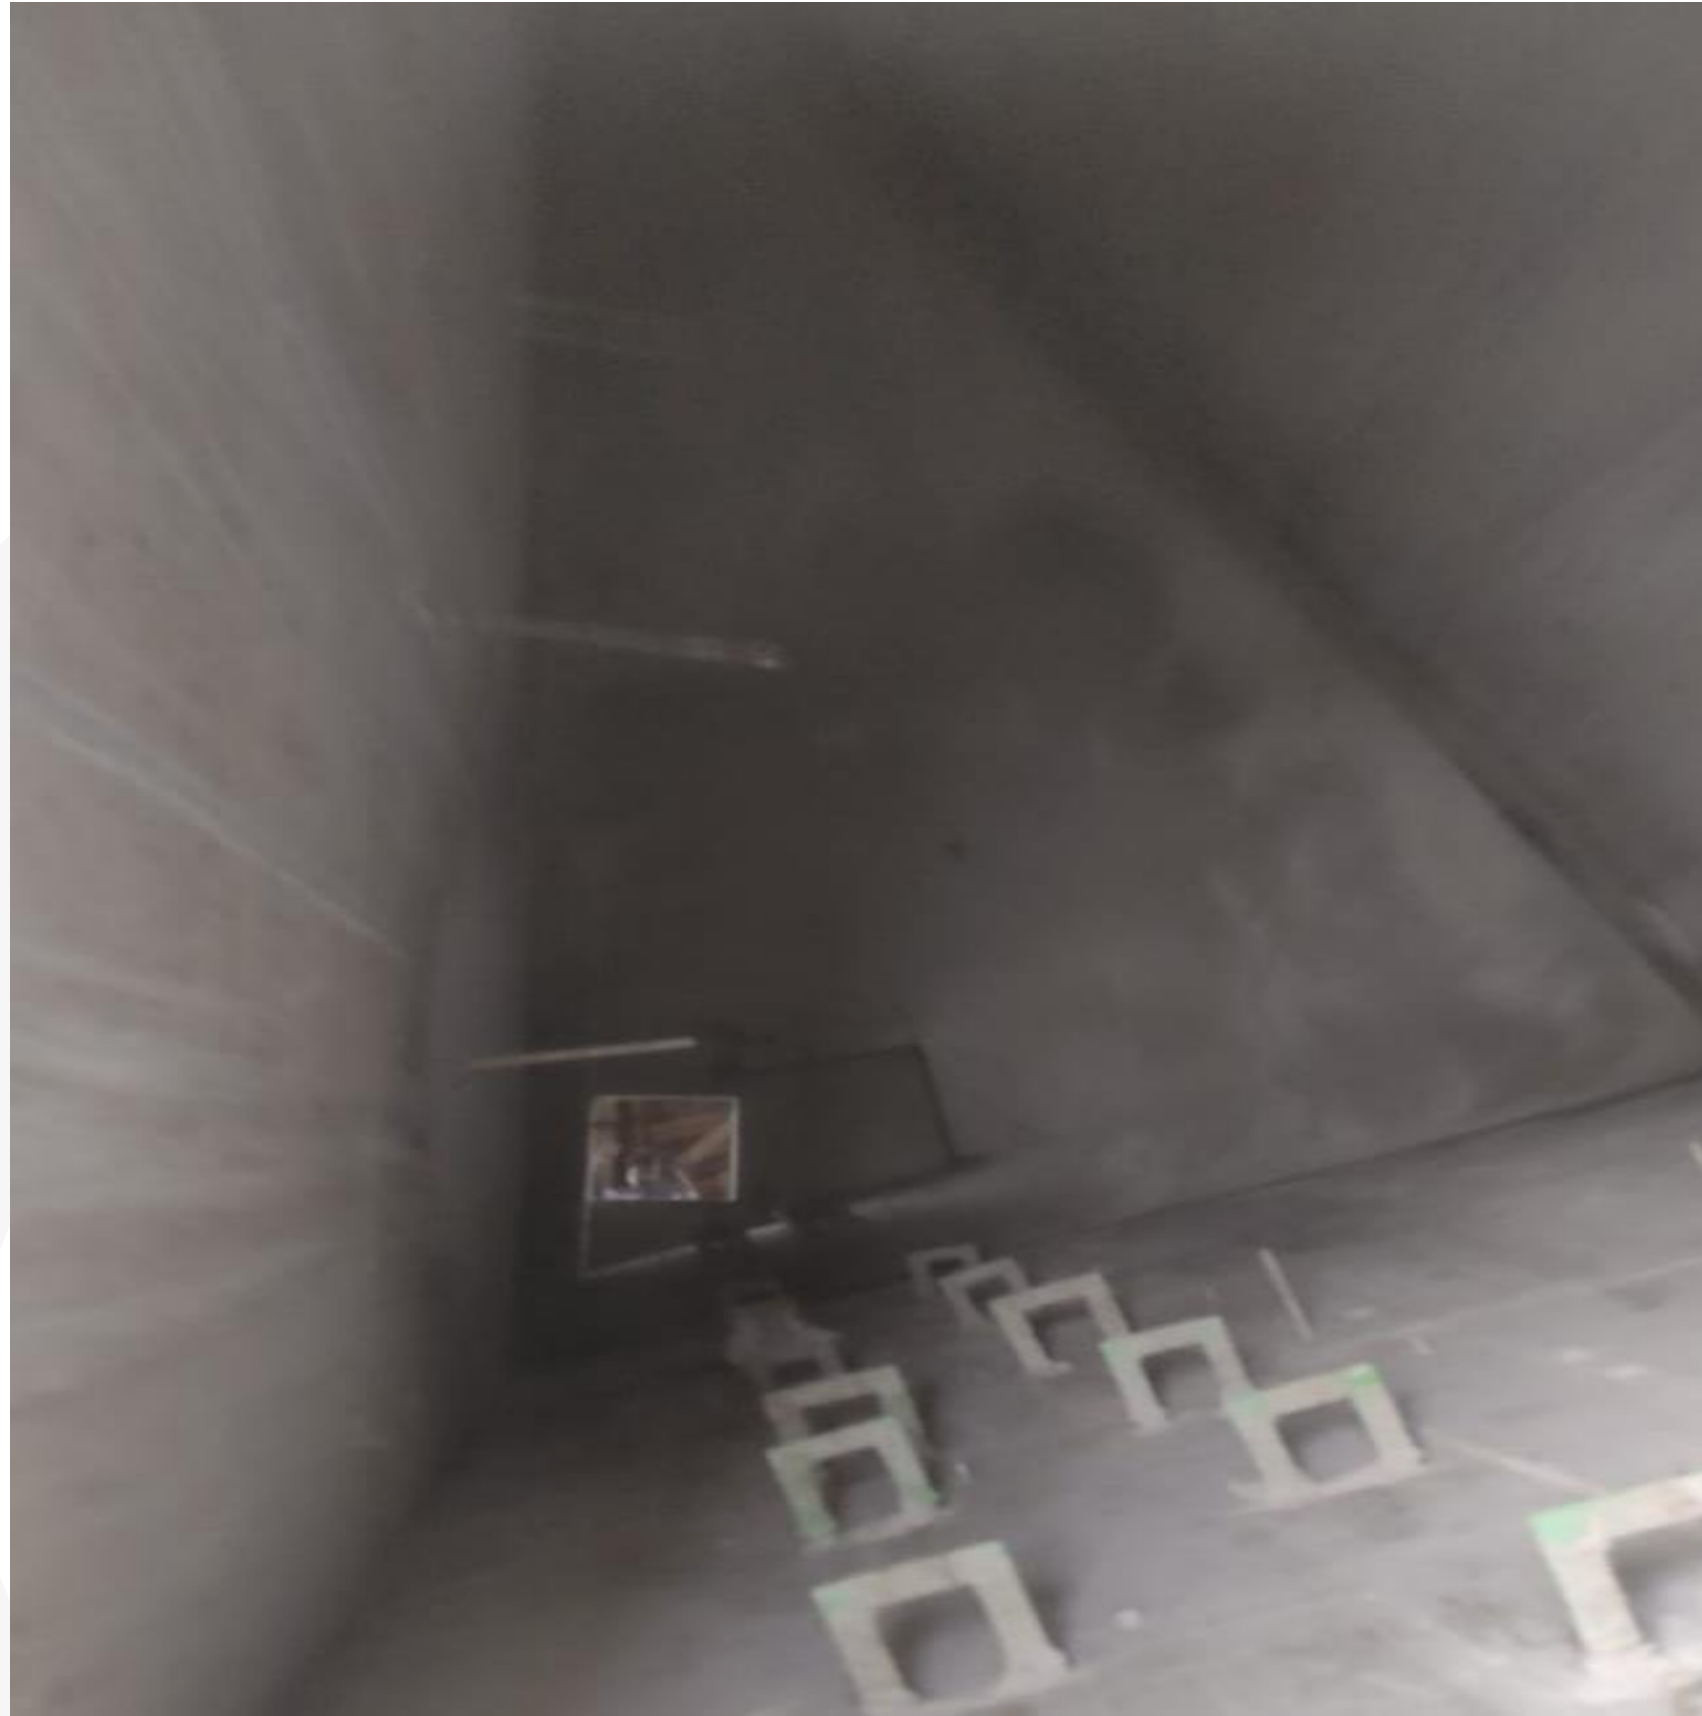

STP – Plum Concrete Work Completed



STP – Inner Tank Waterproofing Work In Progress



Compound wall – Type-1 Excavation completed & Pilecap Work In Progress



Compound wall – Type-6 2nd Lift Concrete Completed



Main Building – West Side View



Main Building –Northwest Side View



Main Building –East Side View



Main Building - South Side View



Main Building - North Side View

*Thank
you!*
