



DRA INFINIQUE CONSTRUCTION UPDATES AUGUST - 24

STAGE COMPLETION STATUS UP TO Aug '24

S. No	Description	Status	Remarks
1	Completion of Foundation	Completed	
2	Commencement of Stilt Floor Roof		
3	Commencement of Upper Stilt Floor Roof		
4	Commencement of First Floor Roof		
5	Commencement of Third Floor Roof		
6	Commencement of Fifth Floor Roof		
7	Commencement of Seventh Floor Roof		
8	Commencement of Nineth Floor Roof		
9	Commencement of Eleventh Floor Roof		
10	Commencement of Thirteenth Floor Roof		
11	Commencement of Masonry Work		
12	Commencement of Internal Plastering		
13	Commencement of Internal Finishes		



North Side View



South Side View.



North East corner view.



South East corner view.



Basement P-01 UG Sump raft concrete work completed.



Basement P-01 UG Sump raft slab de-shuttering work completed.



Basement P-01 UG Sump raft slab curing work in progress.



Basement Pour 1 raft slab reinforcement work in progress.



Basement P-02 Pile cap & beam reinforcement work in progress.



Basement P-01 UG Sump around area wall reinforcement work in progress.



Basement P-01 Raft Pile cap & beam shuttering work in progress.



Basement P-01 Raft Concrete work completed.



Basement P-01 Raft de-shuttering work completed.



East side retaining wall starter shuttering work completed.




East side retaining wall starter Concrete work completed.



East side retaining wall shuttering work in progress.



Pour - 02 area excavation works.

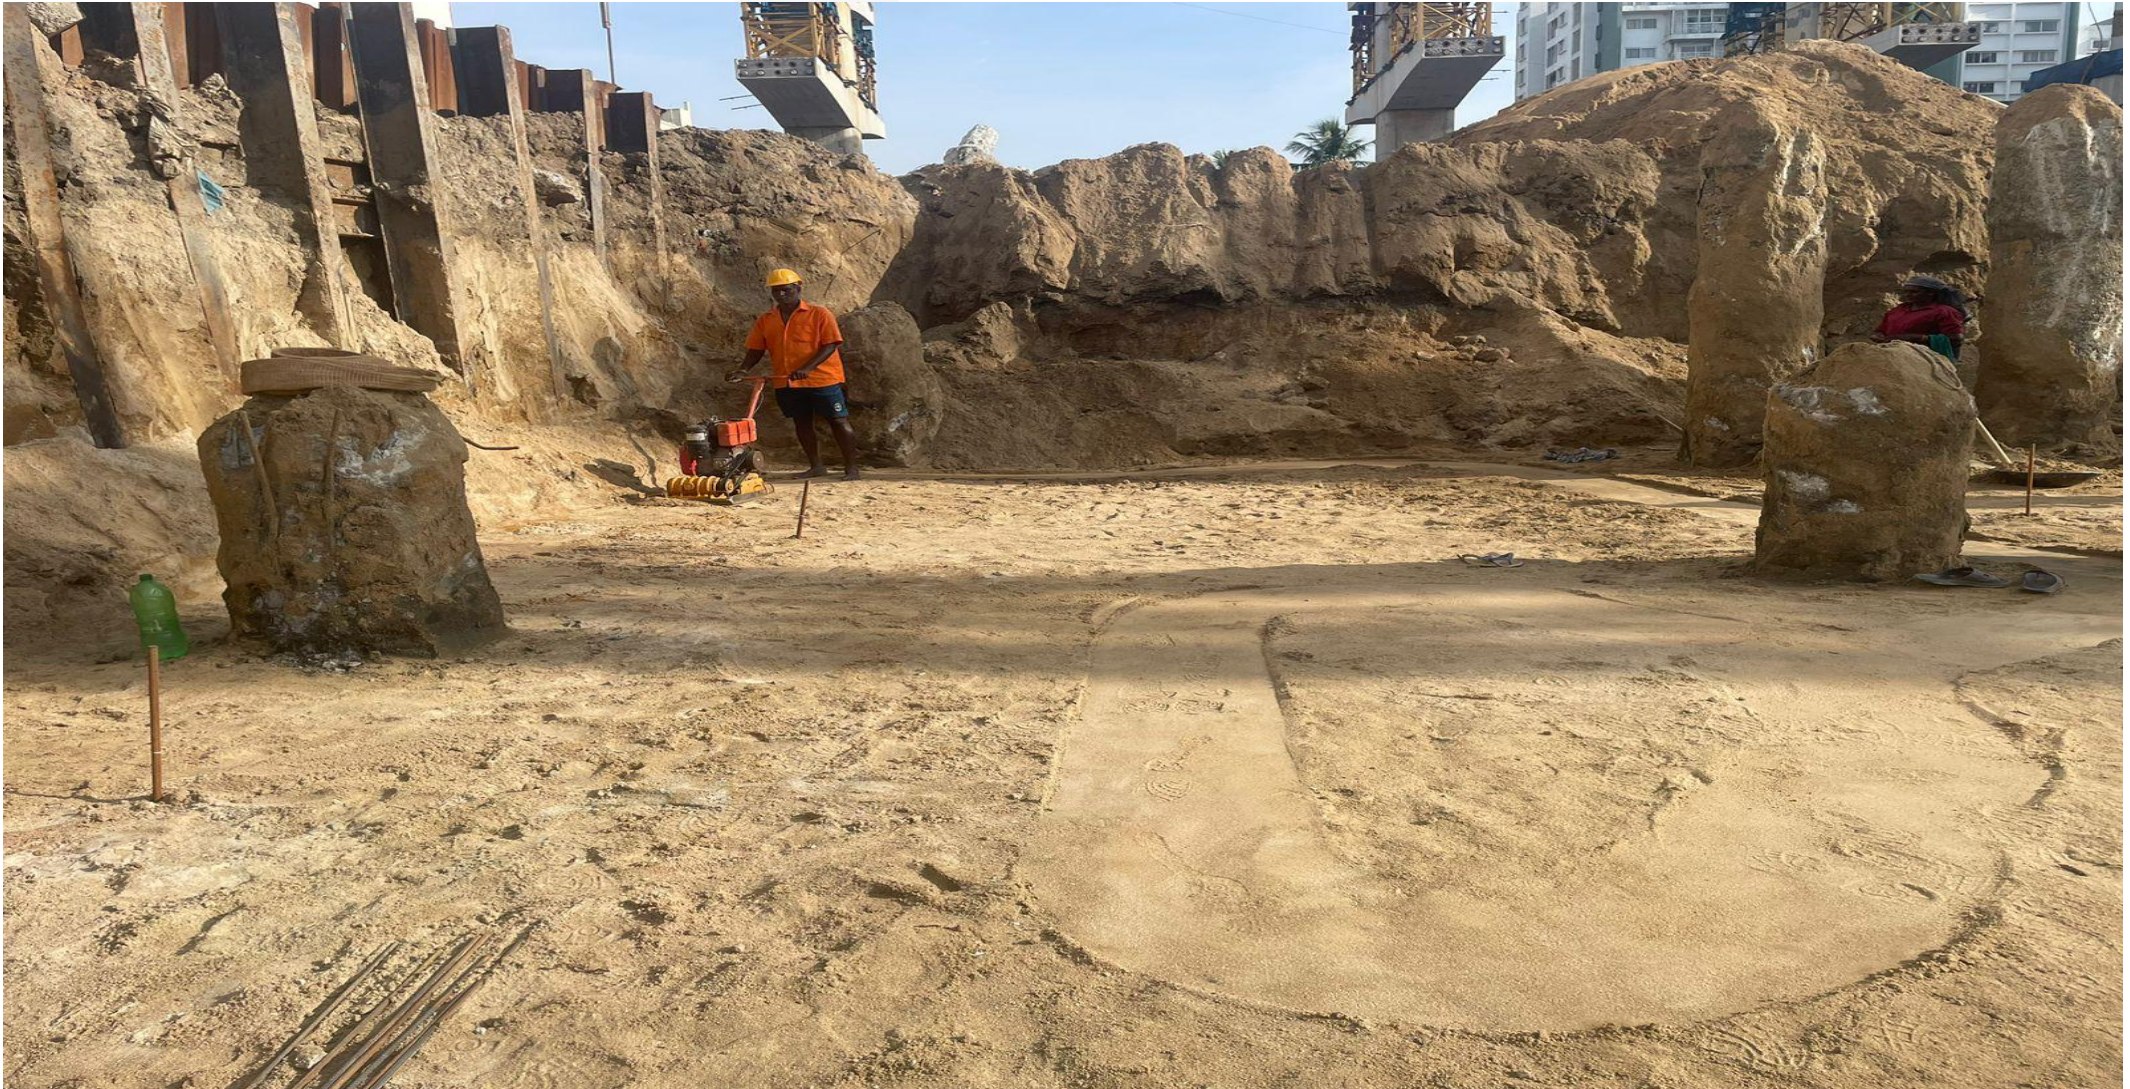

Pour 02 area levelling & compaction works.



Pour 02 area Anti Termite works completed.



Pour -02 & 03 area PCC completed, pile chipping work in progress.



Pour-02 & 03 pile integrity test work completed.



Pour-02 Raft, pile cap & beam reinforcement work in progress.



Pour-02 area shuttering work in progress.



Pour-01 area column reinforcement work in progress.



Sheet pile shoring work completed.



Sales office, foundation work completed.



*Thank
you!*
