



DRA INFINIQUE
CONSTRUCTION UPDATES NOVEMBER -25.



North Side View



East Side View.



South Side View.



Front view.



1st floor toilet concealed tank fixing work in progress



3rd floor bathroom water line work in progress



4th & 5th floor toilet water proofing work in progress



5th floor inner wall plastering work completed



6th floor inner wall plastering work completed



7th floor inner wall electrical pipe laying work completed



7th floor inner wall plastering work in progress.



6th & 7th floor plastering curing works in progress.



9th Floor block work completed.



10th Floor block work in progress.



Pour 1 – 12th Floor roof reinforcement work completed.



Pour 1 12th floor roof slab electrical pipe laying work completed



Pour 1 12th floor roof slab concrete work completed



Pour 1 12th floor roof slab curing work



Pour 2 – 12th floor roof shuttering work completed.



Pour 2 12th floor roof slab reinforcement work completed.




Pour 2 12th floor roof slab electric conduit work completed.



Pour 2 12th floor roof slab concrete work completed.



Pour 1 13th floor column concrete work completed.

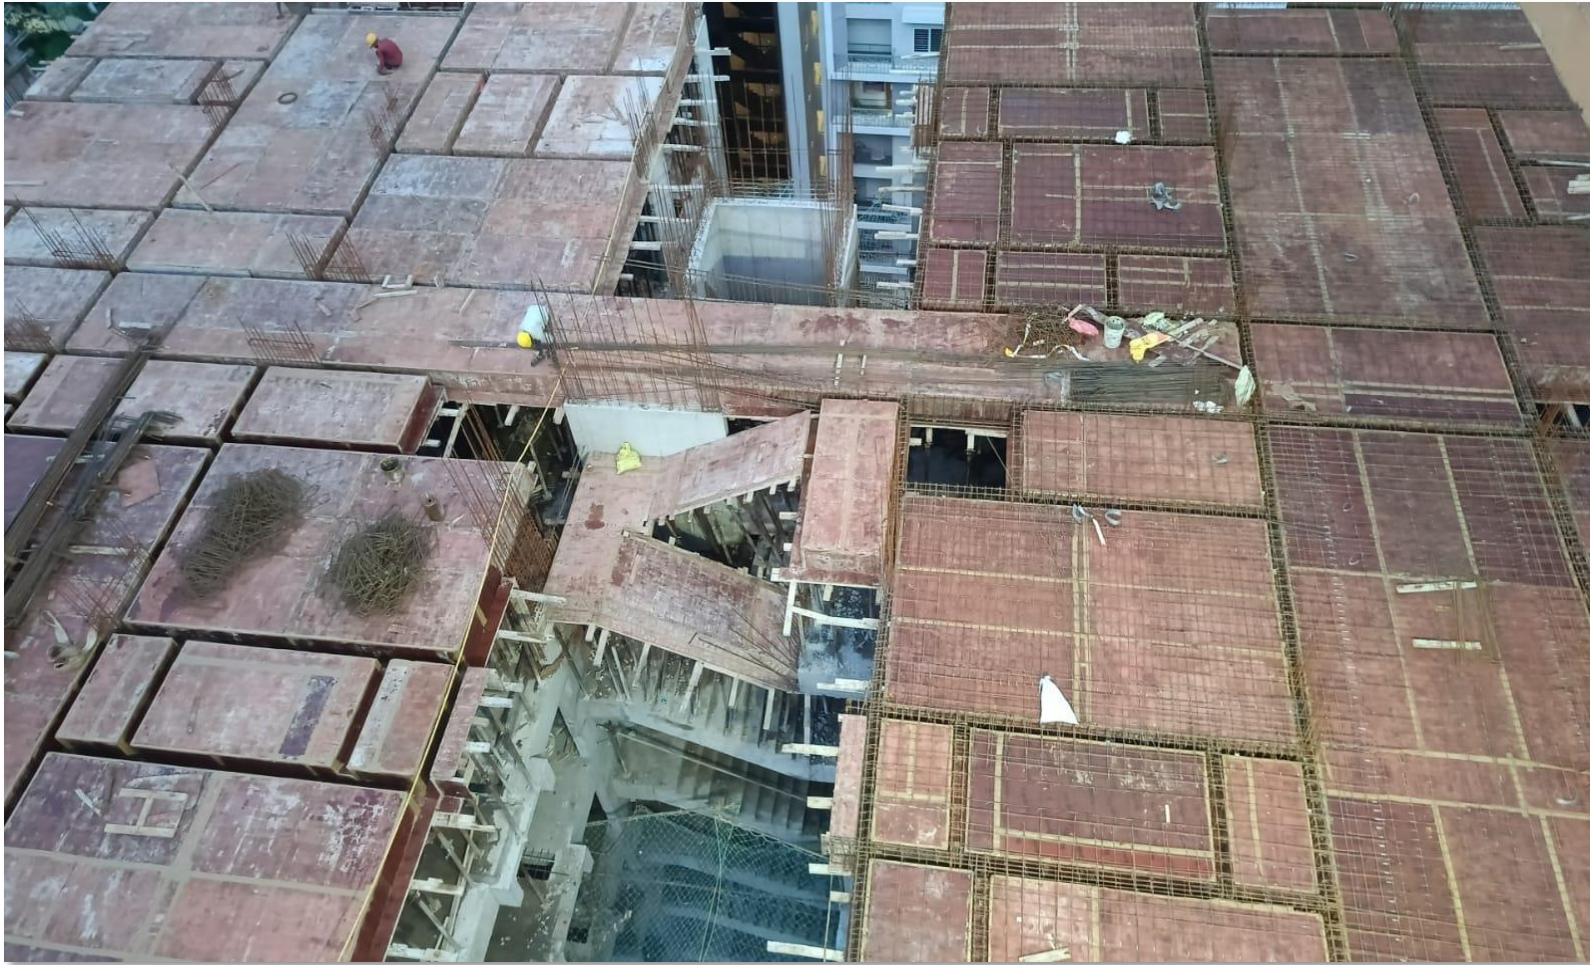

Pour 1 13th floor roof shuttering completed.



Pour 1 13th floor roof reinforcement work completed.



Pour 1 13th floor roof electrical work completed.



Pour 1 13th floor roof concrete work completed.



Pour 2 13th floor column concrete work completed.



Pour 2 13th floor roof shuttering work in progress.



Tower 2 1st floor roof slab reinforcement work completed



Tower 2 1st floor PT work completed



Tower 2 1st floor roof slab concrete work completed



Tower 2 1st floor roof slab curing work completed.



Tower 2 1st floor roof PT Stressing work completed.



Tower - 2 2nd floor column concrete work in progress.

DRA INFINIQUE PROJECT COMPLETION UPDATES

S NO	Description	Unit	Total qty	Completed qty	% of Completion
1	T-1 Basement roof slab	Cum	497	497	100%
2	T-1 First floor roof slab	Cum	216	216	100%
3	T-1 Second floor roof slab	Cum	216	216	100%
4	T-1 Third floor roof slab	Cum	220	220	100%
5	T-1 Fourth floor roof slab	Cum	220	220	100%
6	T-1 Fifth floor roof slab	Cum	220	220	100%
7	T-1 Sixth floor roof slab	Cum	220	200	100%
8	T-1 Seventh floor roof slab	Cum	220	220	100%
9	T-1 Eighth floor roof slab	Cum	220	220	100%
10	T-1 Ninth floor roof slab	Cum	220	220	100%
11	T-1 Tenth floor roof slab	Cum	220	220	100%
12	T-1 Eleventh floor roof slab	Cum	220	220	100%
13	T-1 Twelfth floor roof slab	Cum	220	220	100%
14	T-1 Thirteenth floor roof slab	Cum	248	158	65%
15	T-2 P1 Basement roof slab	Cum	198	198	100%
16	T-2 Stilt roof slab	Cum	125	125	100%
17	T-2 first floor roof slab	Cum	125	125	100%

*Thank
you!*
