

DRA POLARIS MONTHLY CONSTRUCTION PHOTOS – JUNE 2026



Content

- ❖ Master Plan
- ❖ Structure –Progress Status & Photos
 - ✓ Shell & Core
 - ✓ Block Work
 - ✓ Plastering
- ❖ Finishing –Progress Status & Photos
 - ✓ Toilet Waterproofing
 - ✓ Tile Laying
 - ✓ Painting
 - ✓ MEP Work
 - ✓ Upvc Windows
 - ✓ Joinery
- ❖ External Development

DRA POLARIS				
PROGRESS TRACKING SHEET				
S.No	Activity	Block -01	Block -02	Remarks
1	Excavation	Completed	Completed	
2	Foundation	Completed	Completed	
3	Plinth Beam	Completed		
4	Back Filling	Completed		
5	Stilt Floor -Column	Completed		
6	Stilt Floor Roof Slab	Completed		
7	First Floor			
	Column	Completed		
	Roof Slab	Completed		
	Block Work	Work in progress		
	Plastering -Internal			
8	Second Floor			
	Column	Completed		
	Roof Slab	Completed		
	Block Work	Completed		
	Plastering -Internal	Completed		
9	Third Floor			
	Column	Completed		
	Roof Slab	Completed		
	Block Work	Completed		
	Plastering -Internal	Completed		
10	Fourth Floor			
	Column	Completed		
	Roof Slab	Completed		
	Block Work	Completed		
	Plastering -Internal	Work in progress		

Page 1

DRA POLARIS				
PROGRESS TRACKING SHEET				
S.No	Activity	Block -01	Block -02	Remarks
11	Fifth Floor			
	Column	Completed		
	Roof Slab	Completed		
	Block Work	Completed		
	Plastering -Internal	Work in progress		
12	Sixth Floor			
	Column	Completed		
	Roof Slab	Completed		
	Block Work	Work in progress		
	Plastering -Internal			
13	Seventh Floor			
	Column	Completed		
	Roof Slab	Completed		
	Block Work	Work in progress		
	Plastering -Internal			
14	Eighth Floor			
	Column	Completed		
	Roof Slab	Completed		
	Block Work			
	Plastering -Internal			
15	Ninth Floor			
	Column	Completed		
	Roof Slab	Completed		
	Block Work			
	Plastering -Internal			

Page 2

DRA POLARIS				
PROGRESS TRACKING SHEET				
S.No	Activity	Block -01	Block -02	Remarks
16	Tenth Floor			
	Column	Work in progress		
	Roof Slab	Work in progress		
	Block Work			
	Plastering -Internal			
17	Eleventh Floor			
	Column			
	Roof Slab			
	Block Work			

Page 3

MASTER PLAN



Top view



North side elevation



South side elevation



East side elevation



West side elevation



Main building – 9th floor Pour 1 Roof Slab concrete completed



Main building – 9th floor pour 2 roof slab Concrete work completed



Main building – 10th floor Pour 1 roof slab shuttering work in progress



Main building – 10th floor Pour 1 slab reinforcement work in progress




Main building – 10th floor Pour 2 column concrete work completed



Main building – 6th & 7th floor block work in progress



Main building - 4th & 5th floor wall chasing & pipe fixing work in progress

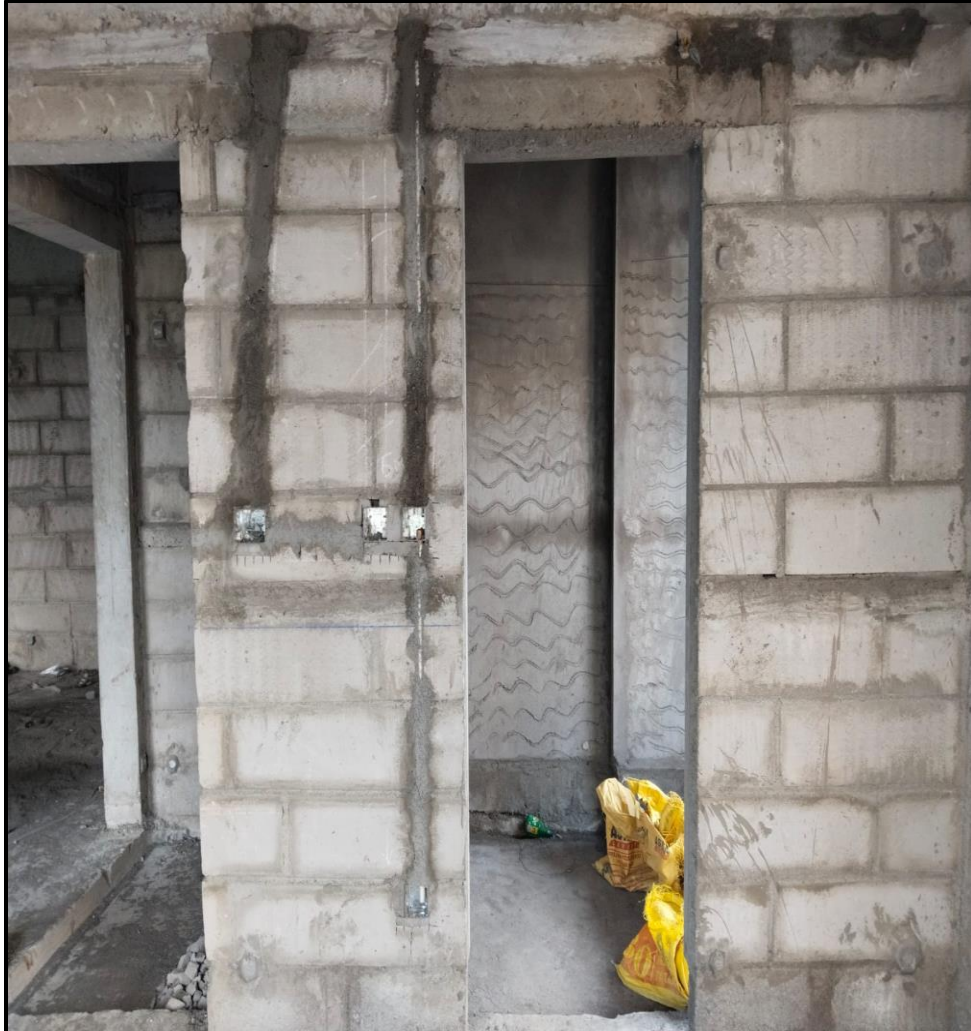

Main building - 4rd floor wall & 5th floor toilet plastering work in progress



Main building – 4th floor toilet core cutting work completed



Main building – 2nd floor toilet waterproofing work in progress (8/20)



*Thank
you!*
